



Crossrail West Stations Newsletter

January 2021

Welcome

Welcome to our latest update on the work we are undertaking to enhance and upgrade a number of stations in West London, ready for the Elizabeth line.

Work continued on each of the six stations over the festive period and we're pleased to let you know that three of the stations (Acton Main Line, West Ealing and Ealing Broadway) are now close to completion and, following all of the necessary safety and quality checks, will be welcoming passengers in the next couple of months.


So, although we start 2021 with another national lockdown, spring is in sight and we are working with our contractors and industry partners to complete these stations, with their upgraded facilities, as soon as possible. Until next time, stay safe and well.

Station by station update



Over the last month we have completed the installation of the external doors and glazing at **West Ealing** and are close to completing the installation of the new concourse ceiling. We have

completed the finishing work on platform 4 and installed the fire doors. The ticket machines and gate line have now been installed and the final testing and commissioning of these will be completed in January.

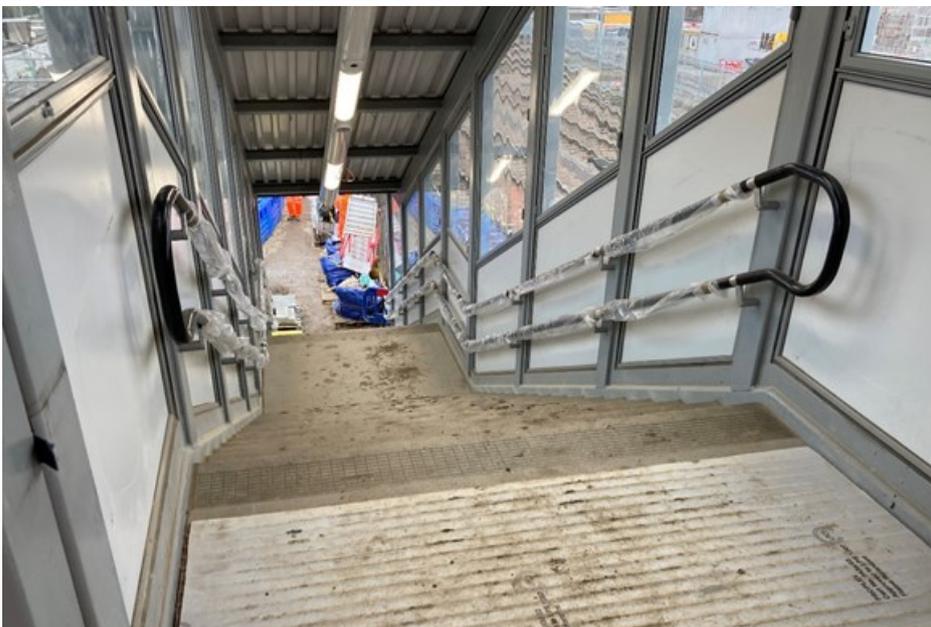

Acton Main Line—handrails and metalwork added to staircases

At **Acton Main Line** we completed the installation of the passenger lifts, ready for their testing and commissioning to take place in January. The resurfacing work for platforms 2/3 and 4 continued and the metalwork and handrails were added to the platform stairs. Internal doors were installed and the glass sliding doors were added to the station entrance, as the work nears completion.

Throughout December we glazed, sealed and painted the new footbridge at **Southall** and continued with site drainage. Work started on the block and brick work for the ground floor internal walls within the new station building.

Cladding continued for the new station building and lift motor rooms, along with the installation of cable trays for new electrics and telecoms equipment.



Southall—passenger lift installation

Lower level roofing works on the **West Drayton** station building extension were completed last month and we started installing electrical and telecoms cabling within the new station concourse.

Installation of the new platform lifts continued, along with mechanical and electrical works within the lift motor rooms. We started work to remove and replace the roof on the existing platform 1 building.



Ealing Broadway—glazing at entrance

At **Ealing Broadway** we continued with the installation of the lifts, with the lift that will serve platform 4 nearing completion.

Work will continue into January to install the lifts for platforms 1, 2/3 as well as the ticket gates and the flooring for the ticket office.

Electrical and mechanical work was carried out over the festive season and continues into January, when work to reinstate the platforms will also take place.



West Drayton—glazing installation

At **Hayes & Harlington** we started the interior brick work and continued with the installation of steelwork for the new station building.

We added roof cladding and continued the installation of the new platform lifts and progressed electrical and drainage works.



Hayes & Harlington—steelwork for new station building



Crossrail West Stations Newsletter

January 2021

Location	What we are doing in February
Acton Main Line	<p>We will be completing the final stages of the ceiling fitting, installing the platform shelters and finishing the platform reinstatement work, testing and commissioning the lifts and electrical work, and undertaking the installation of public realm facilities.</p> <p>We will then be finishing off the final snagging work so that the station can be prepared for hand-over to the train operator and station manager, MTR Elizabeth line.</p>
Ealing Broadway	<p>Throughout January we will be continuing with the installation of the first floor office and toilet facilities, adding roof lighting and cladding, and testing and commissioning the lift that serves platform 4 as well as installing the lift for platform 2/3. We will also be installing the ticket gate and starting the public realm work.</p>
West Ealing	<p>This month we will be installing the ceilings, internal cladding and glazing, as well as undertaking the reinstatement works on platform 2/3. We will also be completing our public realm work, finishing the internal painting and adding anti-graffiti film before moving on to the final snagging work to prepare the station for hand-over to MTR Elizabeth line.</p>
Southall	<p>Site-wide drainage work will be continuing this month, along with the installation of cladding on the new station building and platform steelwork. We will be completing the lift motor room walls on platform 1 and will commence with the installation of the ground floor external blockwork on the new station building. Mechanical and electrical work will commence inside the new station building.</p>
Hayes & Harlington	<p>This month we will complete the installation of the structural steelwork and precast concrete floor slabs for the new station building, along with the installation of the lifts on platforms 1 and 2/3. We will also undertake mechanical and electrical work on the footbridge and platform 1 staircase that leads from the car park. We will also be progressing with the feature wall brickwork along with the installation of roof cladding, blockwork, concrete screed, grouting of the columns and planks within the new station building. Drainage work will be carried out within the footprint of the station and the platforms.</p>
West Drayton	<p>This month we will be installing glazing and curtain walling on the station building extension and will continue with the installation of the electrical and telecoms cabling within the new station concourse. We will also be continuing with the installation of the passenger lifts on platforms 2/3 and 4 as well as the mechanical and electrical works within the lift motor rooms and on the platforms. On the south side of the station the roof on the existing station building on platform 1 will be replaced.</p>

Contact us

If you have a concern or to find out more information:

Email us at CRcrossrail@networkrail.co.uk

Call our 24-hour helpline on **03457 11 41 41**

